

STS CORPORATION COMPANY LIMITED

โครงการ ทางพิเศษฉลองรัช (ส่วนต่อขยาย)

ช่วงจุดโชติ - ถนนลำลูกกา ตอนที่ 3

Main Line (ML) : STA.6+643.949 (BH-08)

Cylinder No: #87930,31,32,33,34,37,38

Design Load : 850 Ton

Type Pile : Bored pile dia. 1500 mm.

Max. Load : 2550 Ton

	D/M/Y	TIME	Maintain (min)	Reading (psi)	Load, Ton	% of Design
Cycle I	18-Jul-26	10:00	0	0	0	0
Max. Load.	18-Jul-26	10:00	60	442	212.50	25
	18-Jul-26	11:00	60	849	425.00	50
	18-Jul-26	12:00	60	1257	637.50	75
	18-Jul-26	13:00	1440	1664	850.00	100
	19-Jul-26	13:00	60	1294	637.50	75
	19-Jul-26	14:00	60	891	425.00	50
	19-Jul-26	15:00	60	488	212.50	25
	19-Jul-26	16:00	60	0	0.00	0
Cycle II	19-Jul-26	17:00	60	442	212.50	25
Max. Load	19-Jul-26	18:00	60	849	425.00	50
	19-Jul-26	19:00	60	1257	637.50	75
	19-Jul-26	20:00	60	1664	850.00	100
	19-Jul-26	21:00	60	2071	1062.50	125
	19-Jul-26	22:00	60	2478	1275.00	150
	19-Jul-26	23:00	60	2885	1487.50	175
	20-Jul-26	00:00	1440	3292	1700.00	200
	21-Jul-26	00:00	60	2905	1487.50	175
	21-Jul-26	01:00	60	2502	1275.00	150
	21-Jul-26	02:00	60	2100	1062.50	125
	21-Jul-26	03:00	60	1697	850.00	100
	21-Jul-26	04:00	60	1294	637.50	75
	21-Jul-26	05:00	60	891	425.00	50
	21-Jul-26	06:00	60	488	212.50	25
	21-Jul-26	07:00	60	0	0.00	0

STS CORPORATION COMPANY LIMITED

โครงการ ทางพิเศษฉลองรัช (ส่วนต่อขยาย)

ช่วงจุดโชติ - ถนนลำลูกกา ตอนที่ 3

Main Line (ML) : STA.6+643.949 (BH-08)

Cylinder No: #87930,31,32,33,34,37,38

Design Load : 850 Ton

Type Pile : Bored pile dia. 1500 mm.

Max. Load : 2550 Ton

	D/M/Y	TIME	Maintain (min)	Reading (psi)	Load, Ton	% of Design
Cycle III	21-Jul-26	08:00	30	442	212.50	25
Max. Load	21-Jul-26	08:30	30	849	425.00	50
	21-Jul-26	09:00	30	1257	637.50	75
	21-Jul-26	09:30	30	1664	850.00	100
	21-Jul-26	10:00	30	2071	1062.50	125
	21-Jul-26	10:30	30	2478	1275.00	150
	21-Jul-26	11:00	30	2885	1487.50	175
	21-Jul-26	11:30	30	3292	1700.00	200
	21-Jul-26	12:00	30	3699	1912.50	225
	21-Jul-26	12:30	30	4107	2125.00	250
	21-Jul-26	13:00	30	4514	2337.50	275
	21-Jul-26	13:30	30	4921	2550.00	300
	21-Jul-26	14:00	30	4517	2337.50	275
	21-Jul-26	14:30	30	4114	2125.00	250
	21-Jul-26	15:00	30	3711	1912.50	225
	21-Jul-26	15:30	30	3308	1700.00	200
	21-Jul-26	16:00	30	2905	1487.50	175
	21-Jul-26	16:30	30	2502	1275.00	150
	21-Jul-26	17:00	30	2100	1062.50	125
	21-Jul-26	17:30	30	1697	850.00	100
	21-Jul-26	18:00	30	1294	637.50	75
	21-Jul-26	18:30	30	891	425.00	50
	21-Jul-26	19:00	30	488	212.50	25
	21-Jul-26	19:30	30	0	0.00	0
	21-Jul-26	20:00	End of Test			

STS CORPORATION COMPANY LIMITED

CALIBRATION OF HYDRAULIC JACKS

Gauge Reading psi	AMSLER CALIBRATED LOAD, TON							
	LOADING							TOTAL
	87930	87931	87932	87933	87934	87937	87938	
0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
500	51.0	47.0	47.0	46.0	45.0	47.0	47.0	330.0
1000	79.0	75.0	75.0	73.0	72.0	74.0	73.0	521.0
1500	108.0	106.0	107.0	104.0	104.0	106.0	104.0	739.0
2000	142.0	139.0	143.0	138.0	136.0	141.0	138.0	977.0
2500	177.0	178.0	180.0	176.0	174.0	177.0	174.0	1236.0
3000	214.0	217.0	220.0	216.0	212.0	216.0	213.0	1508.0
3500	251.0	257.0	263.0	257.0	252.0	258.0	254.0	1792.0
4000	287.0	299.0	303.0	299.0	292.0	298.0	296.0	2074.0
4500	325.0	338.0	343.0	337.0	330.0	338.0	334.0	2345.0
5000	362.0	376.0	384.0	378.0	370.0	377.0	375.0	2622.0
5500	395.0	416.0	421.0	413.0	409.0	414.0	415.0	2883.0
6000	431.0	446.0	453.0	447.0	441.0	447.0	443.0	3108.0

*** LOADING ***

Regression Output:

Constant	-18.33333
Std Err of Y Est	41.79558
R Squared	0.99821
No. of Observations	12
Degrees of Freedom	10

X Coefficient(s)	0.52192
Std Err of Coef.	0.00699

$$\text{Loading} = (0.52192 * \text{Reading}) - 18.33333$$

STS CORPORATION COMPANY LIMITED

CALIBRATION OF HYDRAULIC JACKS

Gauge Reading psi	AMSLER CALIBRATED LOAD, TON							TOTAL
	UNLOADING							
	87930	87931	87932	87933	87934	87937	87938	
0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0
500	59.0	45.0	43.0	42.0	43.0	43.0	44.0	319.0
1000	85.0	70.0	70.0	69.0	69.0	69.0	70.0	502.0
1500	116.0	103.0	102.0	101.0	99.0	98.0	100.0	719.0
2000	149.0	138.0	137.0	135.0	134.0	133.0	137.0	963.0
2500	183.0	175.0	172.0	171.0	169.0	168.0	171.0	1209.0
3000	220.0	217.0	214.0	212.0	210.0	210.0	212.0	1495.0
3500	258.0	259.0	255.0	251.0	251.0	252.0	251.0	1777.0
4000	293.0	300.0	297.0	295.0	292.0	293.0	294.0	2064.0
4500	330.0	340.0	339.0	337.0	333.0	333.0	334.0	2346.0
5000	365.0	381.0	379.0	377.0	374.0	375.0	375.0	2626.0
5500	401.0	420.0	419.0	415.0	411.0	413.0	413.0	2892.0

*** UNLOADING ***

Regression Output:

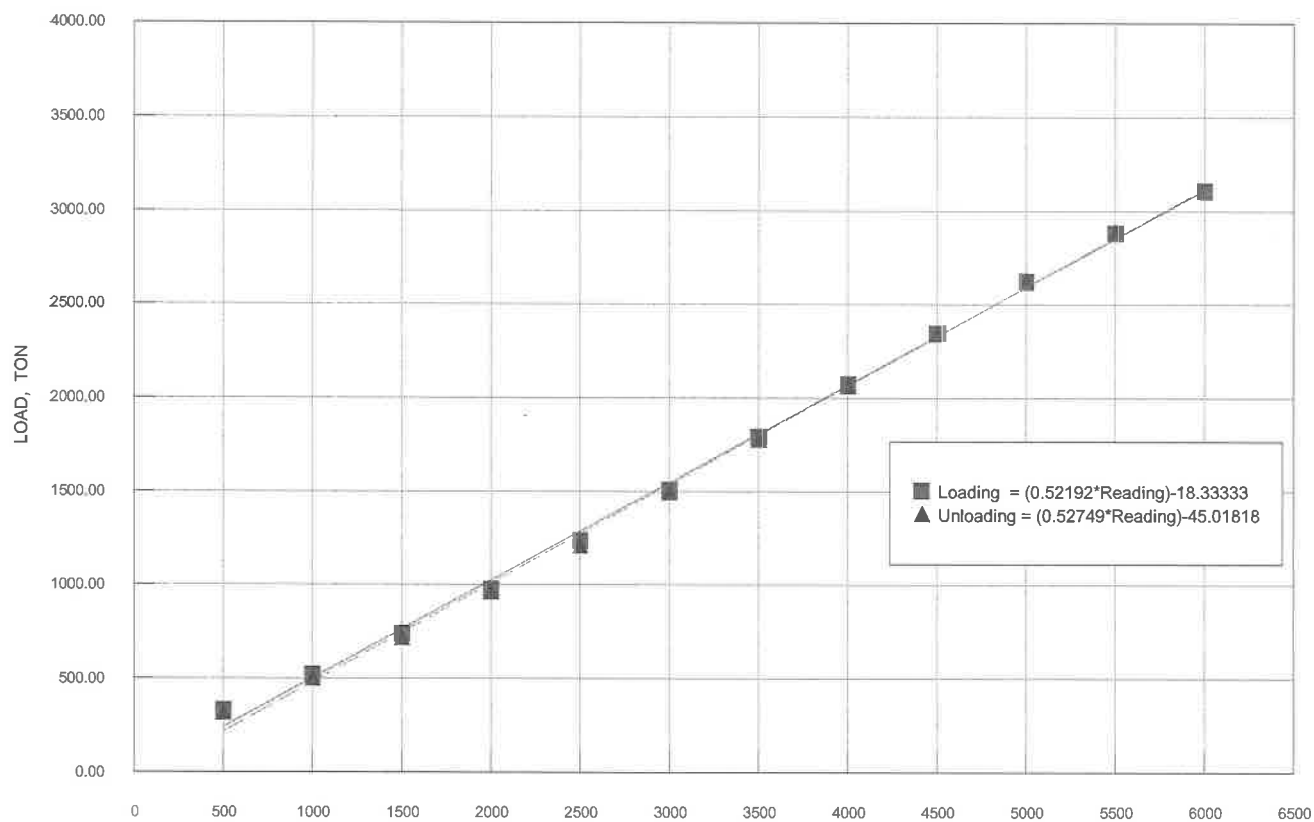
Constant	-45.01818
Std Err of Y Est	50.18588
R Squared	0.99705
No. of Observations	11
Degrees of Freedom	9

X Coefficient(s)	0.52749
Std Err of Coef.	0.00957

Unloading = (0.52749*Reading)-45.01818

CALIBRATION OF HYDRAULIC JACKS

CYLINDER #87930,31,32,33,34,37,38



STS CORPORATION CO., LTD.

CALIBRATION CERTIFICATE

Certificate No. : CLT-HJ-69010

Job No. : 25690051HJ

Request No. : 69006HJ

Client Company Name : STS Corporation Company Limited

Client Company Address : 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description : Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities : Cylinder No. 87930

UUC Condition : Normal

Calibration Mode : Compression, Loading and Unloading direction

Calibration Range : Maximum load 431 tonF

Calibration Date : March 17, 2026

Certificate Issued Date : March 18, 2026

Calibration Environment : Temperature 31.1 °C, Humidity 60 %RH

Reference Standard (STD)

STD Description : Load Cell with Data Logger CR10X No. 5716

STD Identities : Load Cell No. GHL-450T

STD Certificate : MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by :

Thodsaphol
(Mr.Thodsaphol Kruengklang)

Technical Supervisor



Certificate No. : CLT-HJ-69010
Job No. : 25690051HJ
Request No. : 69006HJ
UUC Description : Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities : Cylinder No. 87930

Calibration Mode : Compression, Loading and Unloading direction

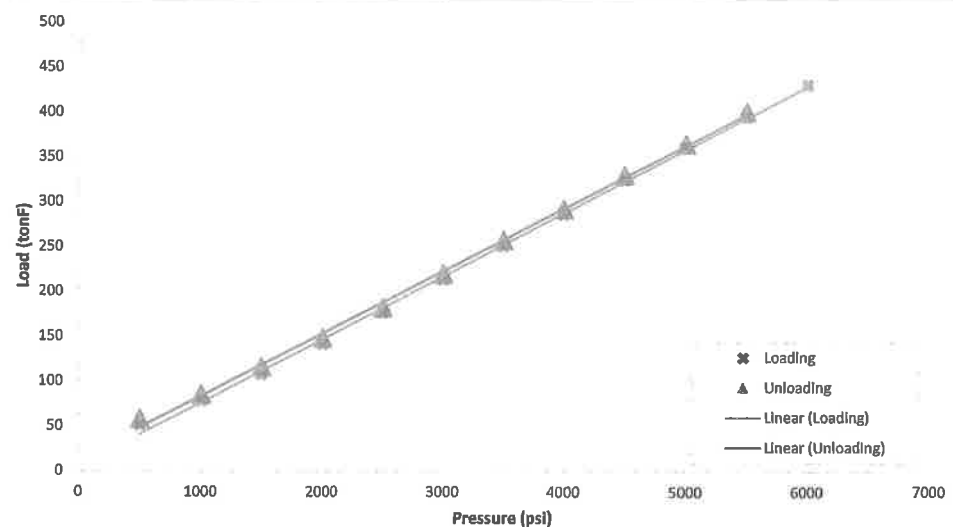
Environment Condition : Temperature 31.1 °C, Humidity 60 %RH

STD Description : Load Cell with Data Logger CR10X No. 5716

STD Identities : Load Cell No. GHL-450T

Calibration Results :

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	53	51	50	51	59	58	59	59
2	1000	79	80	78	79	86	85	85	85
3	1500	108	108	109	108	117	117	116	116
4	2000	142	143	142	142	149	149	148	149
5	2500	177	177	177	177	183	182	183	183
6	3000	215	215	213	214	220	220	221	220
7	3500	251	252	250	251	257	258	258	258
8	4000	288	287	287	287	292	292	293	293
9	4500	326	324	324	325	330	331	331	330
10	5000	362	362	361	362	366	365	364	365
11	5500	395	395	396	395	401	401	400	401
12	6000	430	431	431	431	-	-	-	-

Calibration Curve :

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A * X(\text{psi}) + B$		
	Coefficient :	A	B
	Coefficient Unit :	(tonF/psi)	(tonF)
	Loading :	0.0705	6.2296
	Unloading :	0.0697	14.4144

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68051

Job No.: 25680143HJ

Request No.: 68015HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87931

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 446 tonF

Calibration Date: August 7, 2025

Certificate Issued Date: August 8, 2025

Environment Condition: Temperature 34.0 °C, Humidity 58 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:


(Mr.Thodsaphol Kruengklang)

Technical Supervisor



Certificate No.: CLT-HJ-68051

Job No.: 25680143HJ

Request No.: 68015HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87931

Calibration Mode: Compression, Loading and Unloading direction

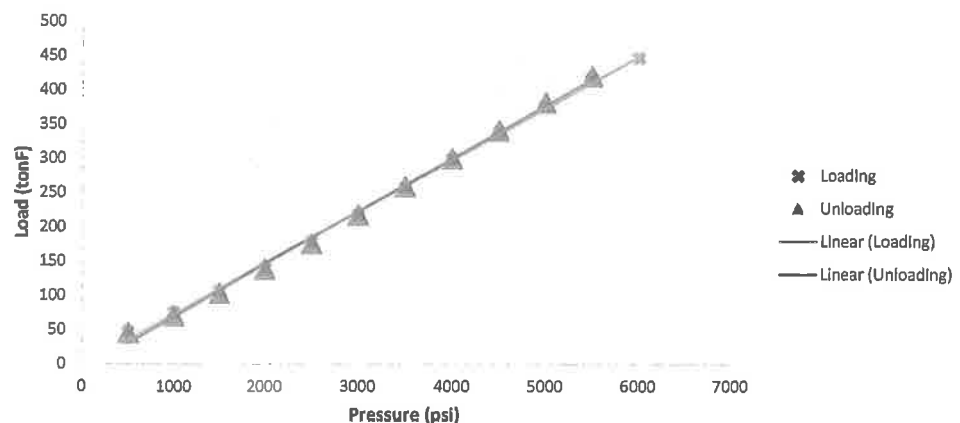
Environment Condition: Temperature 34.0 °C, Humidity 58 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	46	47	46	47	45	45	44	45
2	1000	74	74	75	75	68	71	70	70
3	1500	105	107	106	106	104	103	103	103
4	2000	140	139	139	139	137	137	138	138
5	2500	178	177	178	178	174	175	176	175
6	3000	216	218	216	217	218	216	218	217
7	3500	257	258	256	257	260	259	258	259
8	4000	299	299	299	299	300	300	300	300
9	4500	339	337	338	338	340	340	341	340
10	5000	376	377	376	376	380	382	382	381
11	5500	414	416	416	416	420	419	420	420
12	6000	446	447	446	446	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A * X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0752	-3.4450
	Unloading:	0.0771	-8.8360

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68063

Job No.: 25680172HJ

Request No.: 68019HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87932

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 453 tonF

Calibration Date: October 1, 2025

Certificate Issued Date: October 2, 2025

Environment Condition: Temperature 33.7 °C, Humidity 59 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T


STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:


(Mr.Thodsaphol Kruengklang)
Technical Supervisor

Certificate No.: CLT-HJ-68063

Job No.: 25680172HJ

Request No.: 68019HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87932

Calibration Mode: Compression, Loading and Unloading direction

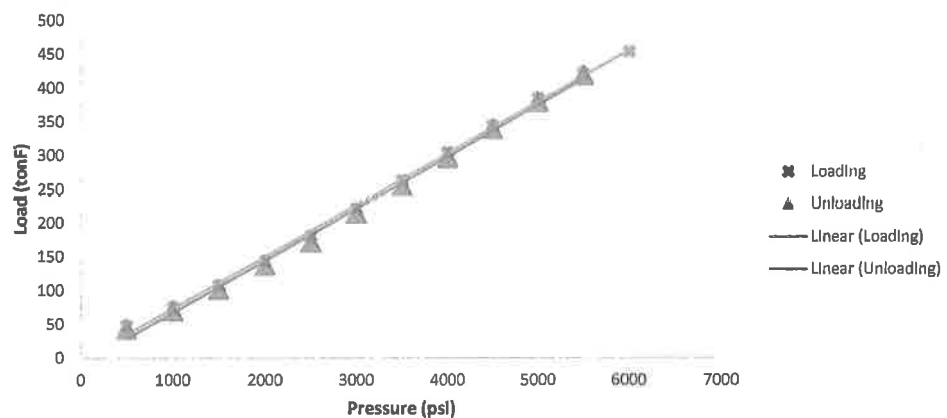
Environment Condition: Temperature 33.7 °C, Humidity 59 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	47	47	48	47	44	43	43	43
2	1000	74	75	75	75	70	70	70	70
3	1500	107	107	106	107	103	102	101	102
4	2000	143	144	143	143	137	138	137	137
5	2500	180	181	181	180	171	172	173	172
6	3000	220	221	220	220	213	215	215	214
7	3500	263	263	262	263	254	256	255	255
8	4000	304	303	303	303	296	297	297	297
9	4500	344	343	343	343	338	339	340	339
10	5000	383	384	384	384	378	380	380	379
11	5500	421	420	420	421	419	418	419	419
12	6000	453	453	453	453	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A \cdot X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0764	-3.3440
	Unloading:	0.0769	-9.8715

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68064

Job No.: 25680172HJ

Request No.: 68019HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87933

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 447 tonF

Calibration Date: October 1, 2025

Certificate Issued Date: October 2, 2025

Environment Condition: Temperature 33.6 °C, Humidity 61 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:


(Mr.Thodsaphol Kruengklang)

Technical Supervisor

Certificate No.: CLT-HJ-68064

Job No.: 25680172HJ

Request No.: 68019HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87933

Calibration Mode: Compression, Loading and Unloading direction

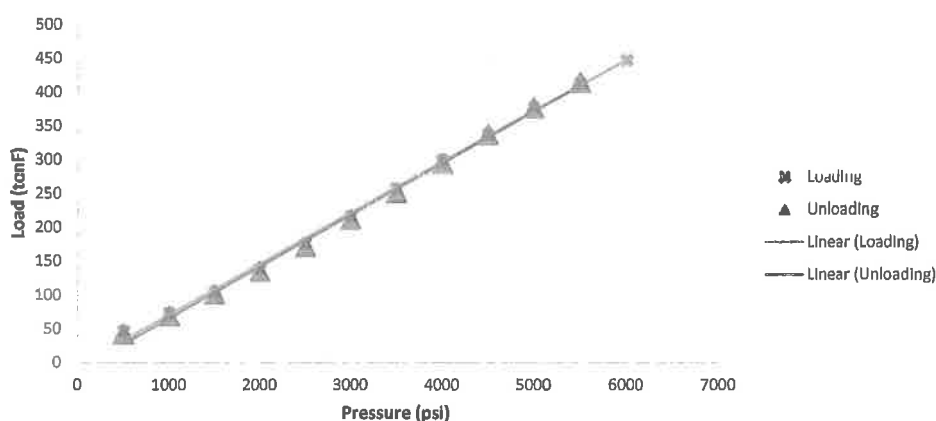
Environment Condition: Temperature 33.6 °C, Humidity 61 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	46	46	46	46	42	42	42	42
2	1000	72	74	73	73	70	68	69	69
3	1500	105	103	105	104	101	101	101	101
4	2000	138	138	138	138	136	134	135	135
5	2500	177	175	176	176	172	171	171	171
6	3000	215	216	216	216	211	212	212	212
7	3500	256	257	258	257	252	250	251	251
8	4000	300	299	299	299	295	296	294	295
9	4500	337	337	336	337	336	337	337	337
10	5000	376	378	378	378	377	376	377	377
11	5500	412	413	414	413	414	415	416	415
12	6000	447	448	447	447	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A \cdot X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0755	-4.8784
	Unloading:	0.0764	-10.6721

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68065

Job No.: 25680172HJ

Request No.: 68019HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87934

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 441 tonF

Calibration Date: October 1, 2025

Certificate Issued Date: October 2, 2025

Environment Condition: Temperature 31.6 °C, Humidity 71 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:

Thodsaphol
(Mr.Thodsaphol Kruengklang)
Technical Supervisor



Certificate No.: CLT-HJ-68065

Job No.: 25680172HJ

Request No.: 68019HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87934

Calibration Mode: Compression, Loading and Unloading direction

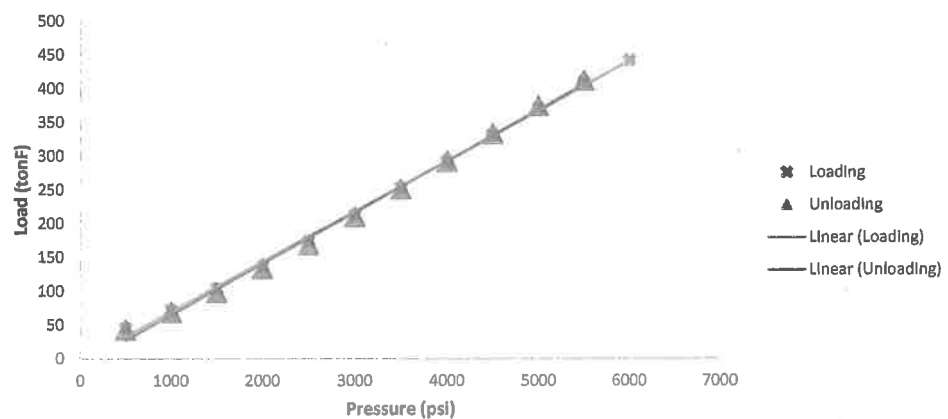
Environment Condition: Temperature 31.6 °C, Humidity 71 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	45	45	45	45	43	42	43	43
2	1000	72	72	72	72	69	68	69	69
3	1500	104	103	104	104	97	99	99	99
4	2000	136	137	136	136	134	135	133	134
5	2500	173	174	175	174	168	169	168	169
6	3000	212	212	214	212	211	210	210	210
7	3500	252	252	253	252	252	250	251	251
8	4000	291	291	293	292	292	291	292	292
9	4500	330	330	331	330	333	332	333	333
10	5000	370	369	371	370	374	374	373	374
11	5500	409	410	408	409	411	410	412	411
12	6000	441	441	441	441	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A \cdot X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0742	-4.7076
	Unloading:	0.0757	-10.5047

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68052

Job No.: 25680143HJ

Request No.: 68015HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87937

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 447 tonF

Calibration Date: August 7, 2025

Certificate Issued Date: August 8, 2025

Environment Condition: Temperature 32.4 °C, Humidity 67 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:


(Mr.Thodsaphol Kruengklang)
Technical Supervisor



Certificate No.: CLT-HJ-68052

Job No.: 25680143HJ

Request No.: 68015HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87937

Calibration Mode: Compression, Loading and Unloading direction

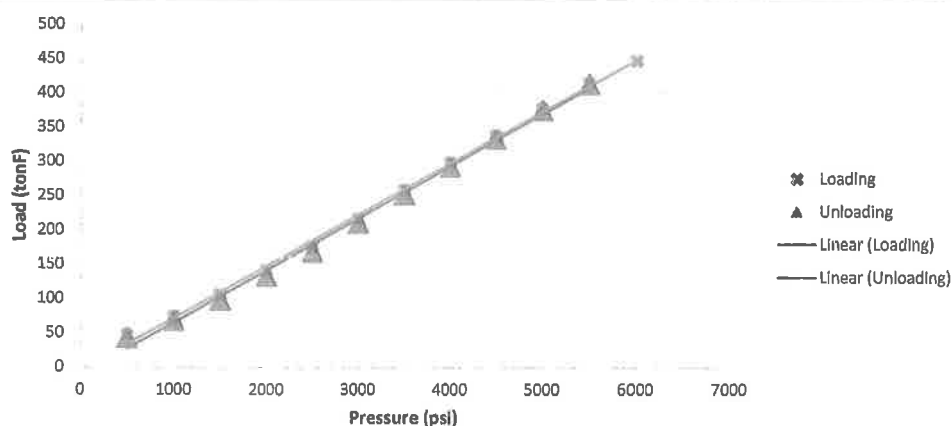
Environment Condition: Temperature 32.4 °C, Humidity 67 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	47	47	46	47	43	43	45	43
2	1000	73	73	75	74	69	70	68	69
3	1500	107	105	106	106	98	97	99	98
4	2000	140	140	141	141	133	133	133	133
5	2500	177	176	177	177	168	167	169	168
6	3000	216	216	217	216	210	210	210	210
7	3500	258	259	259	258	251	253	252	252
8	4000	297	298	299	298	294	293	291	293
9	4500	338	338	337	338	332	333	334	333
10	5000	376	377	377	377	374	376	376	375
11	5500	415	414	413	414	413	414	413	413
12	6000	447	448	446	447	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A * X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0752	-3.4995
	Unloading:	0.0760	-10.9840

- End of certification -

CALIBRATION CERTIFICATE

Certificate No.: CLT-HJ-68049

Job No.: 25680142HJ

Request No.: 68014HJ

Client Company Name: STS Corporation Company Limited

Client Company Address: 196/8-12 Soi Pradipat 14, Pradipat Road, Phayathai, Phayathai, Bangkok 10400

Unit Under Calibration (UUC)

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87938

UUC Condition: Normal

Calibration Mode: Compression, Loading and Unloading direction

Calibration Range: Maximum load 443 tonF

Calibration Date: August 7, 2025

Certificate Issued Date: August 8, 2025

Environment Condition: Temperature 34.0 °C, Humidity 59 %RH

Reference Standard (STD)

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

STD Certificate: MTC 23-67/0229-01

Remark(s) : - The certificate apply only to the identified item above.

- The certificate shall not be reproduced except in full without The written approval of The company.

- Laboratory is not responsible for interpretation or using of calibration results.

Certified by:

(
Mr.Thodsaphol Kruengklang
Technical Supervisor



Certificate No.: CLT-HJ-68049

Job No.: 25680142HJ

Request No.: 68014HJ

UUC Description: Hydraulic Jack with Pressure Gauge No. 537-A and Pump No. 1

UUC Identities: Cylinder No. 87938

Calibration Mode: Compression, Loading and Unloading direction

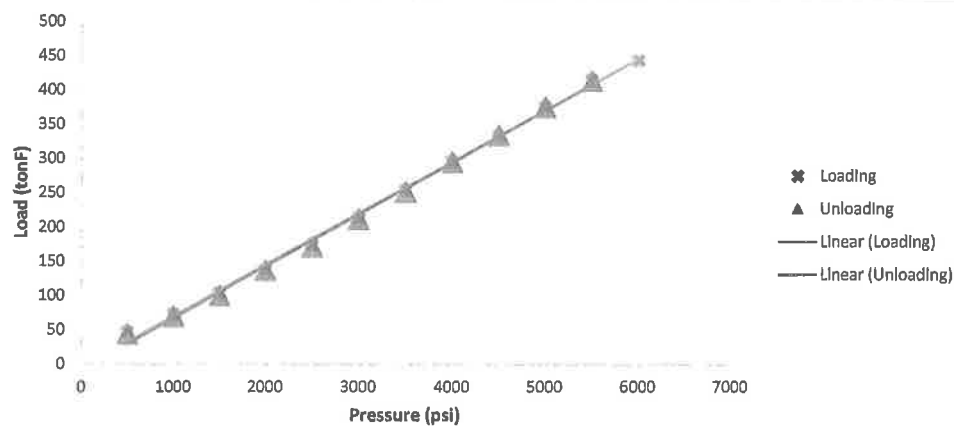
Environment Condition: Temperature 34.0 °C, Humidity 59 %RH

STD Description: Load Cell with Data Logger CR10X No. 5716

STD Identities: Load Cell No. GHL-450T

Calibration Results:

No.	Calibration Point (psi)	UUC Reading (tonF)							
		Loading				Unloading			
		R1	R2	R3	Average	R1	R2	R3	Average
1	500	47	47	47	47	45	44	43	44
2	1000	73	73	74	73	69	70	71	70
3	1500	104	104	103	104	99	101	101	100
4	2000	137	138	137	138	137	136	138	137
5	2500	174	174	174	174	171	170	172	171
6	3000	214	212	212	213	212	211	211	212
7	3500	255	254	254	254	250	251	252	251
8	4000	296	297	296	296	293	295	296	294
9	4500	334	332	335	334	334	333	335	334
10	5000	375	376	375	375	376	374	374	375
11	5500	415	415	416	415	414	412	413	413
12	6000	443	444	443	443	-	-	-	-

Calibration Curve:

Conversion Equations :

Linearity Sensitivity Factor	$Y(\text{tonF}) = A \cdot X(\text{psi}) + B$		
	Coefficient:	A	B
	Coefficient Unit:	(tonF/psi)	(tonF)
	Loading:	0.0750	-5.0257
	Unloading:	0.0756	-8.4285

- End of certification -
